W2026 MAD317-01 Mobile App Project Development (Kayode Olukayode)

Study TO DO – Sprint Planning & Progress Logs

Darshilkumar Karkar
(A00203357)

Repository: https://github.com/darshil2711/Study-TODO

1. Sprint Setup

- Sprint Duration

This sprint took place during 7 days (1 week).

- Sprint Team

This project has been done on an individual basis. The tasks were delegated in the following manner:

  - Product Owner: Darshilkumar Karkar.
  - Scrum Master: Darshilkumar Karkar.
  - Developer: Darshilkumar Karkar.
  - UI/UX Designer: Darshilkumar Karkar.

2. Sprint Planning

A. Sprint Goal

This sprint would design and develop the fundamentals of task management in the Study TO DO mobile application using the Flutter framework.

At the sprint completion, the application can allow the users to:

- Add new study tasks
- View a list of tasks
- Navigate between screens

This provides the basic functionality needed in a study planner application and lays groundwork of future extensions of the system like notifications and data holding.

B. Product Backlog (Sprint selection)

- User Story 1

I, as a student, would like to introduce a new task so that I could keep track of my assignments.

  - Acceptance Criteria:
    - User can enter a task title
    - User can save the task
    - Task appears in the task list
  - Priority: High
  - Roughly Speaking: 5 Story Points.

- User Story 2

As a student, I would like to see everything that I am doing in order to be able to manage my workload.

  - Acceptance Criteria:
    - Tasks are displayed in a list
    - Relevant information (title) is displayed in each task.
  - Priority: High
  - Roughly Speaking: 5 Story Points.

- User Story 3

As a user, I would desire straight forward and clean interface to enable me to use the application.

  - Acceptance Criteria:
    - Layout is clear and readable
    - Buttons are functional
    - UI is based on the material design.
  - Priority: Medium
  - Effort: 3 Story Points (estimated).

- User Story 4

As a user, I would desire the ability of navigation between screens to enable me move through the application without any hassle.

  - Acceptance Criteria:
    - Home screen loads correctly
    - Add Task screen opens without an error.
    - The navigation Back is functional.
  - Priority: High
  - Effort: 3 Story Points (estimated).

C. Sprint Backlog & Task Breakdown

- User Story 1 – Task Creation

Task	Owner	Effort	Status
Design Add Task UI	Self	2 hours	Done
Implement input fields	Self	2 hours	Done
Implement save functionality	Self	3 hours	Done

- User Story 2 – Task List Display

Task	Owner	Effort	Status
Design task list UI	Self	2 hours	Done
Display tasks dynamically	Self	3 hours	Done

- User Story 3 – UI Design

Task	Owner	Effort	Status
Apply Material Design styling	Self	2 hours	Done
Improve layout spacing	Self	1 hours	Done

- User Story 4 – Navigation

Task	Owner	Effort	Status
Configure navigation routes	Self	2 hours	Done
Implement screen transitions	Self	2 hours	Done

D. Sprint Planning Evidence

The project management tool (a project management tool can be GitHub Projects or Trello) was used to make a sprint planning board divided into:

  - To Do
  - In Progress
  - Done
- Evidence Included:
  - Screenshot of sprint board
  - Screenshot of backlog items

3. Sprint Planning

- Day 1
  - Date: Day 1
  - Sprint Day: 1
  - Tasks Worked On:
    - Flutter project setup
    - Initial folder structure
  - Progress:
    - Project is successfully started.
    - Basic app screen created
  - Blockers:
    - None
  - Next Steps:
    - Start UI design input of tasks.

- Day 2
  - Tasks Worked On:
    - Designed Add Task screen
  - Progress:
    - UI layout completed
  - Blockers:
    - Minor alignment issues
  - Next Steps:
    - Install input functionality.

- Day 3
  - Tasks Worked On:
    - When task input fields are implemented.
  - Progress:
    - The functionality of user input works.
  - Blockers:
    - Small state management disorientation.
  - Next Steps:
    - Implement task saving logic

- Day 4
  - Tasks Worked On:
    - Enacted task saving logic.
  - Progress:
    - Tasks successfully were added to list.
  - Blockers:
    - Startup-non persistent data.
  - Next Steps:
    - Improve data handling

- Day 5
  - Tasks Worked On:
    - Task list UI implementation
  - Progress:
    - Activities presented in dynamism.
  - Blockers:
    - UI refresh delay
  - Next Steps:
    - Optimize UI performance

- Day 6
  - Tasks Worked On:
    - Navigation implementation
  - Progress:
    - Screen navigation ought to be functional.
  - Blockers:
    - Back navigation problem was fixed.
  - Next Steps:
    - Final UI improvements

- Day 7
  - Tasks Worked On:
    - Final testing and debugging
  - Progress:
    - Application stable, functional.
  - Blockers:
    - None
  - Next Steps:
    - Make documentation and submission.

4. Evidence of work

The process of development is supported by the following facts:

- History of commits on GH, indicating gradual development.
- View of operational features.
- Screen shots of the application in the emulators.
- Task board updates

5. Sprint Review Summary

- Sprint Goal Review

This sprint was aimed at the implementation of the main task management of the Study TO DO application.

- Completed Work
  - Task creation feature
  - Task list display
  - Navigation system

- Incomplete Work
  - Storing of data (to be done in future sprint)

- Conclusion

The sprint objective was also attained. The application takes its central functionality and offers a good basis to build on.

6. Sprint Retrospective

- Start
  - Local database (Hive or SQLite) Implementation.
  - Add notification system
-
- Stop
  - Wasting the time on the perfection of the UI at an early stage.
-
- Continue
  - After systematic task planning.
  - Record keeping of progress on a daily basis.

7. Improvements

- Process Improvement:
  - Planning accuracy should be enhanced by making the estimation of the task duration more accurate.

- Technical Improvement:
  - Use a better method of state management (e.g., Provider or Riverpod) to be more scalable.

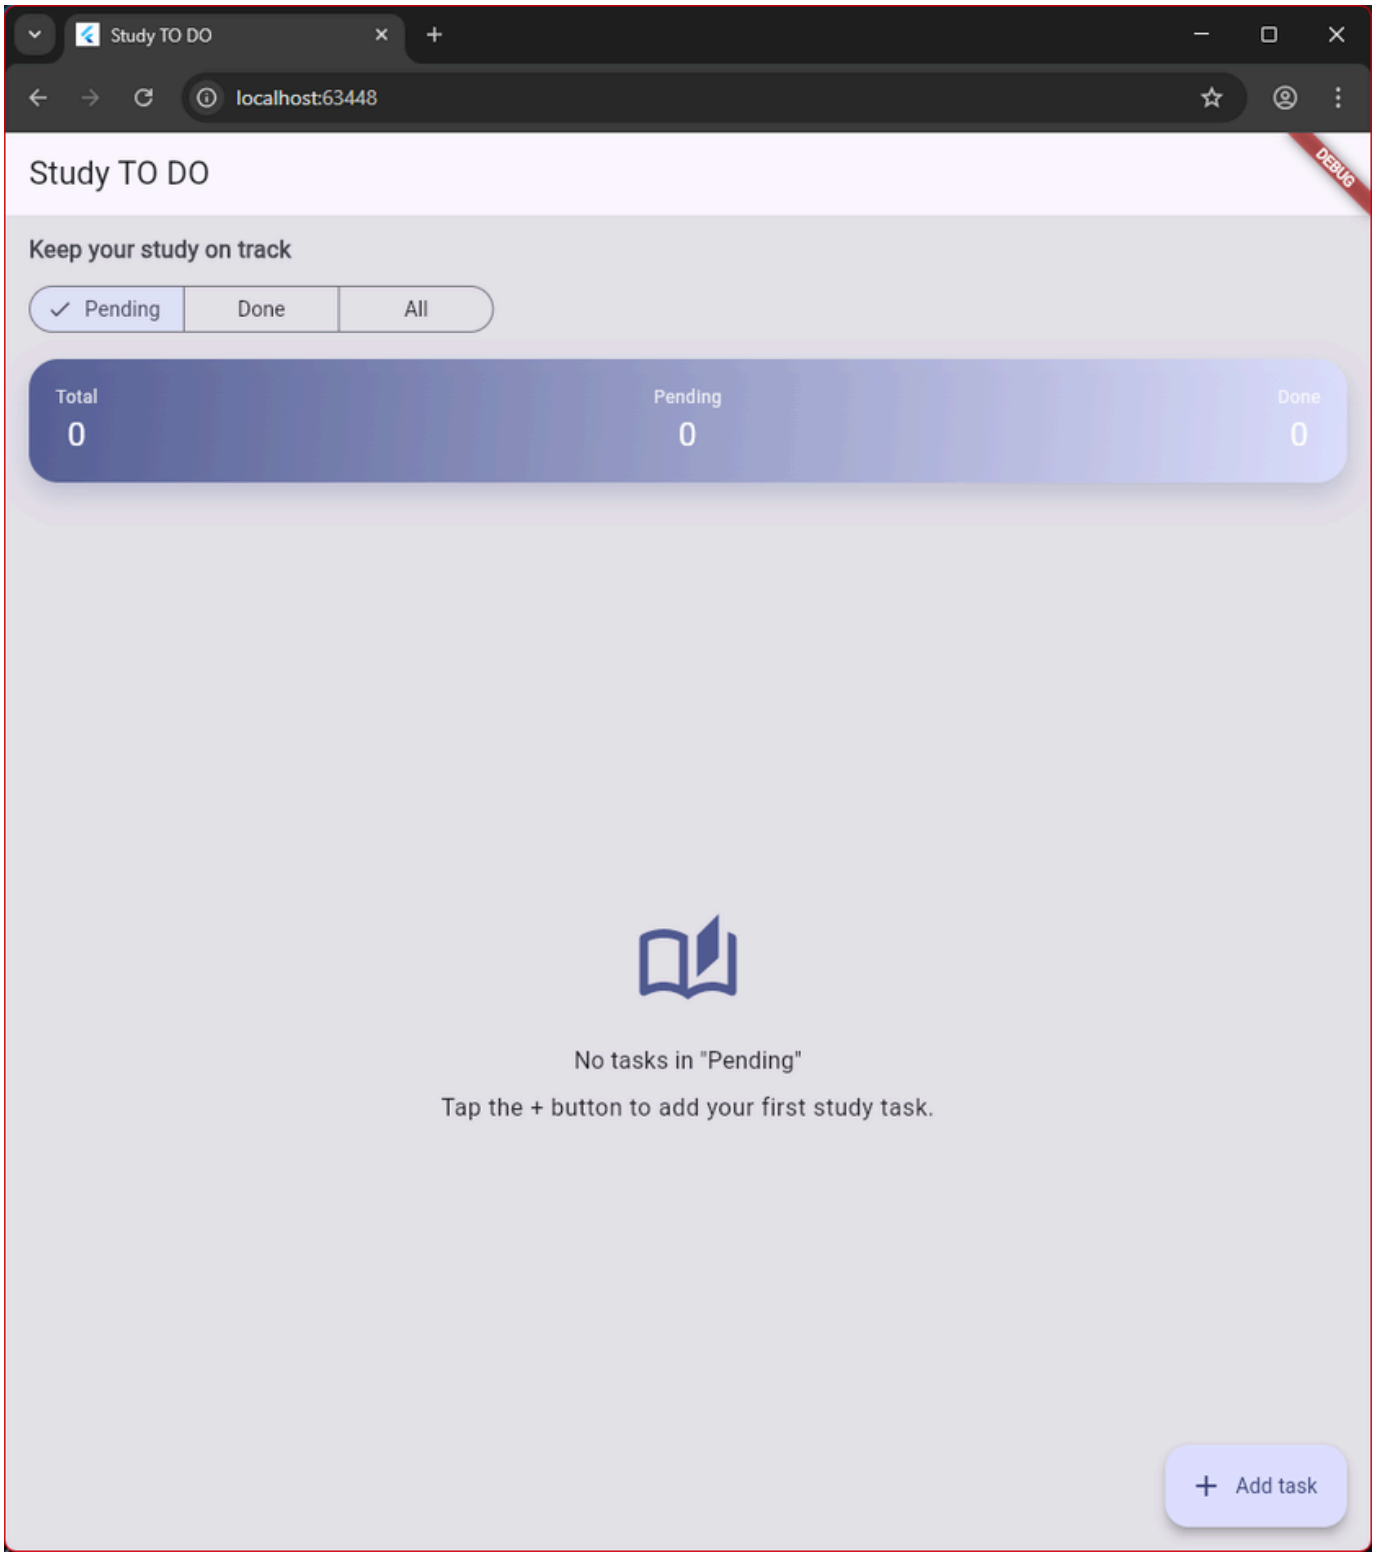
Study TO DO
localhost:63448
Study TO DO
DEBUG
Keep your study on track
Pending
Done
All
Total
0
Pending
0
Done
0
No tasks in "Pending"
Tap the + button to add your first study task.
Add task

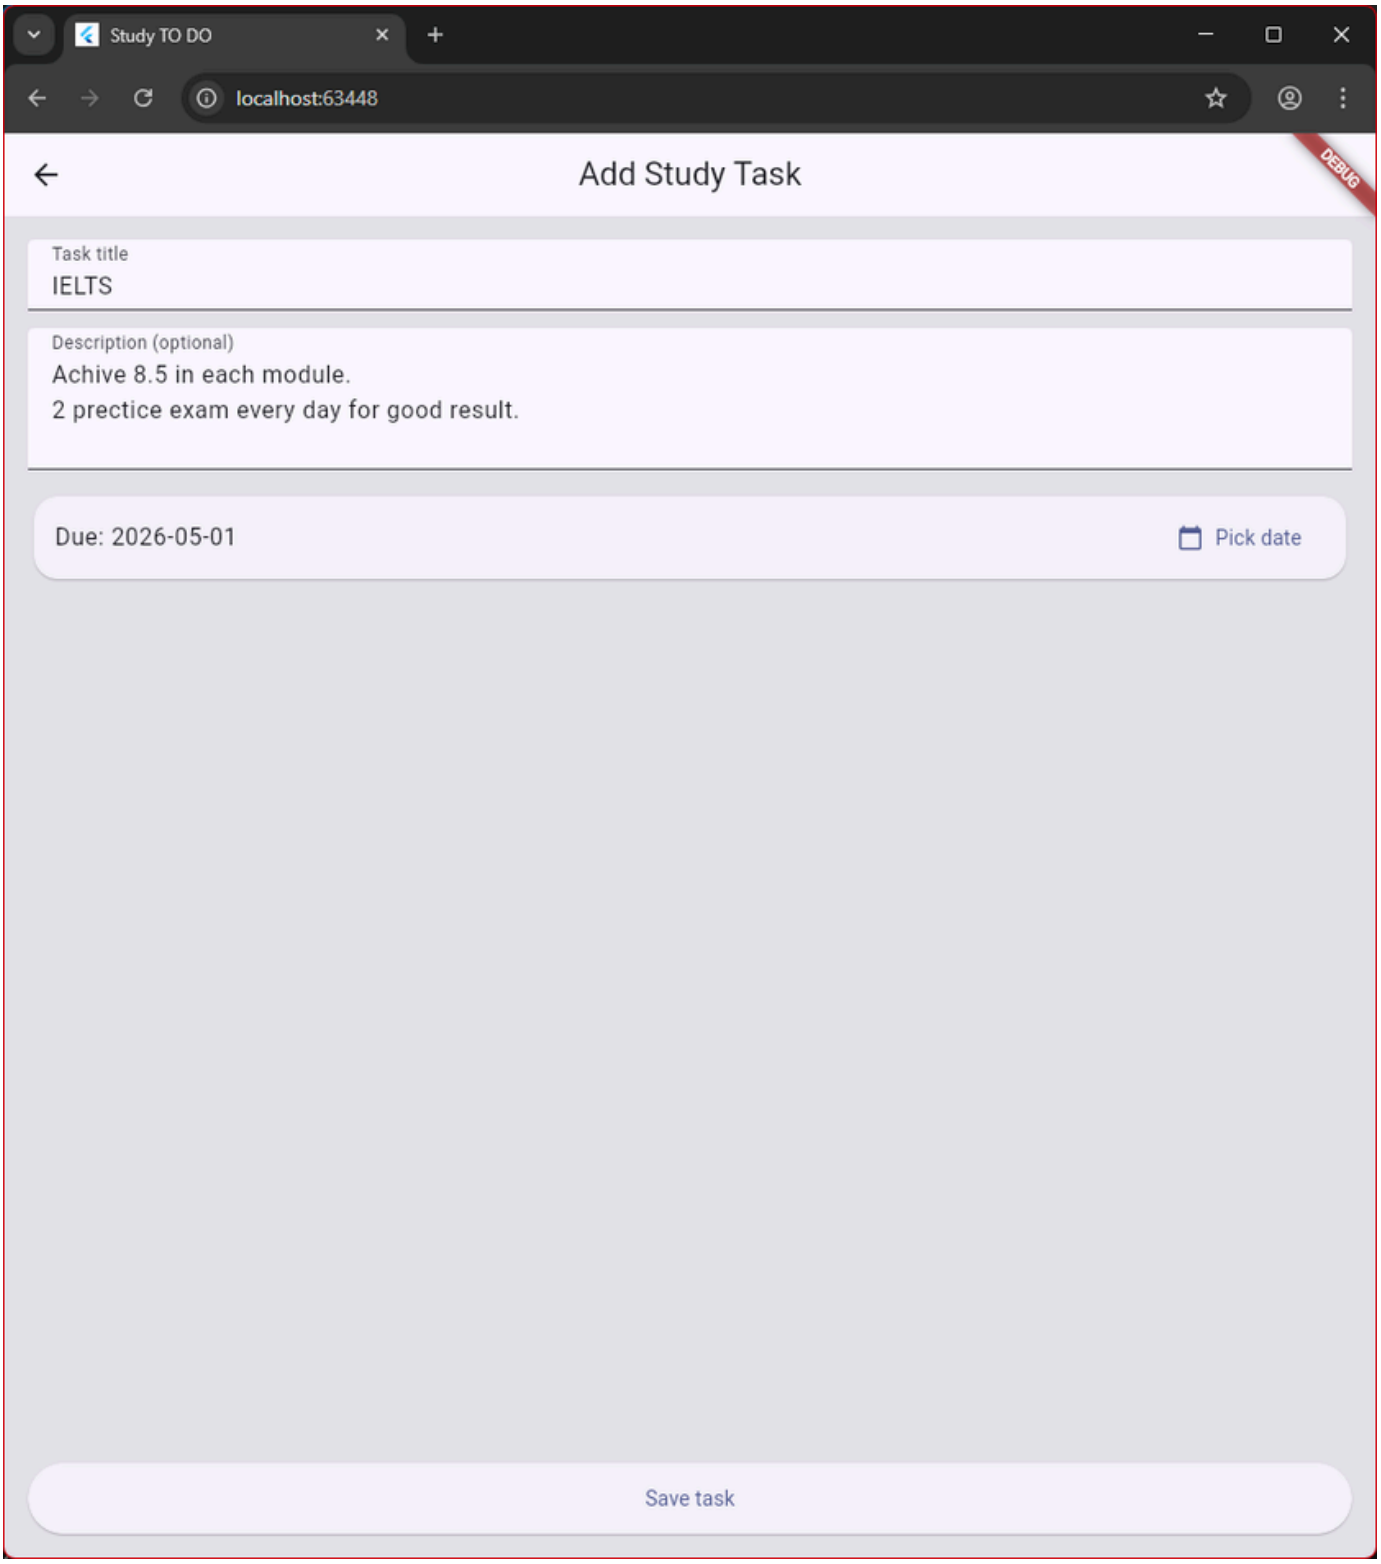
Study TO DO
localhost:63448
Add Study Task
DEBUG
Task title
IELTS
Description (optional)
Achive 8.5 in each module.
2 prectice exam every day for good result.
Due: 2026-05-01
Pick date
Save task

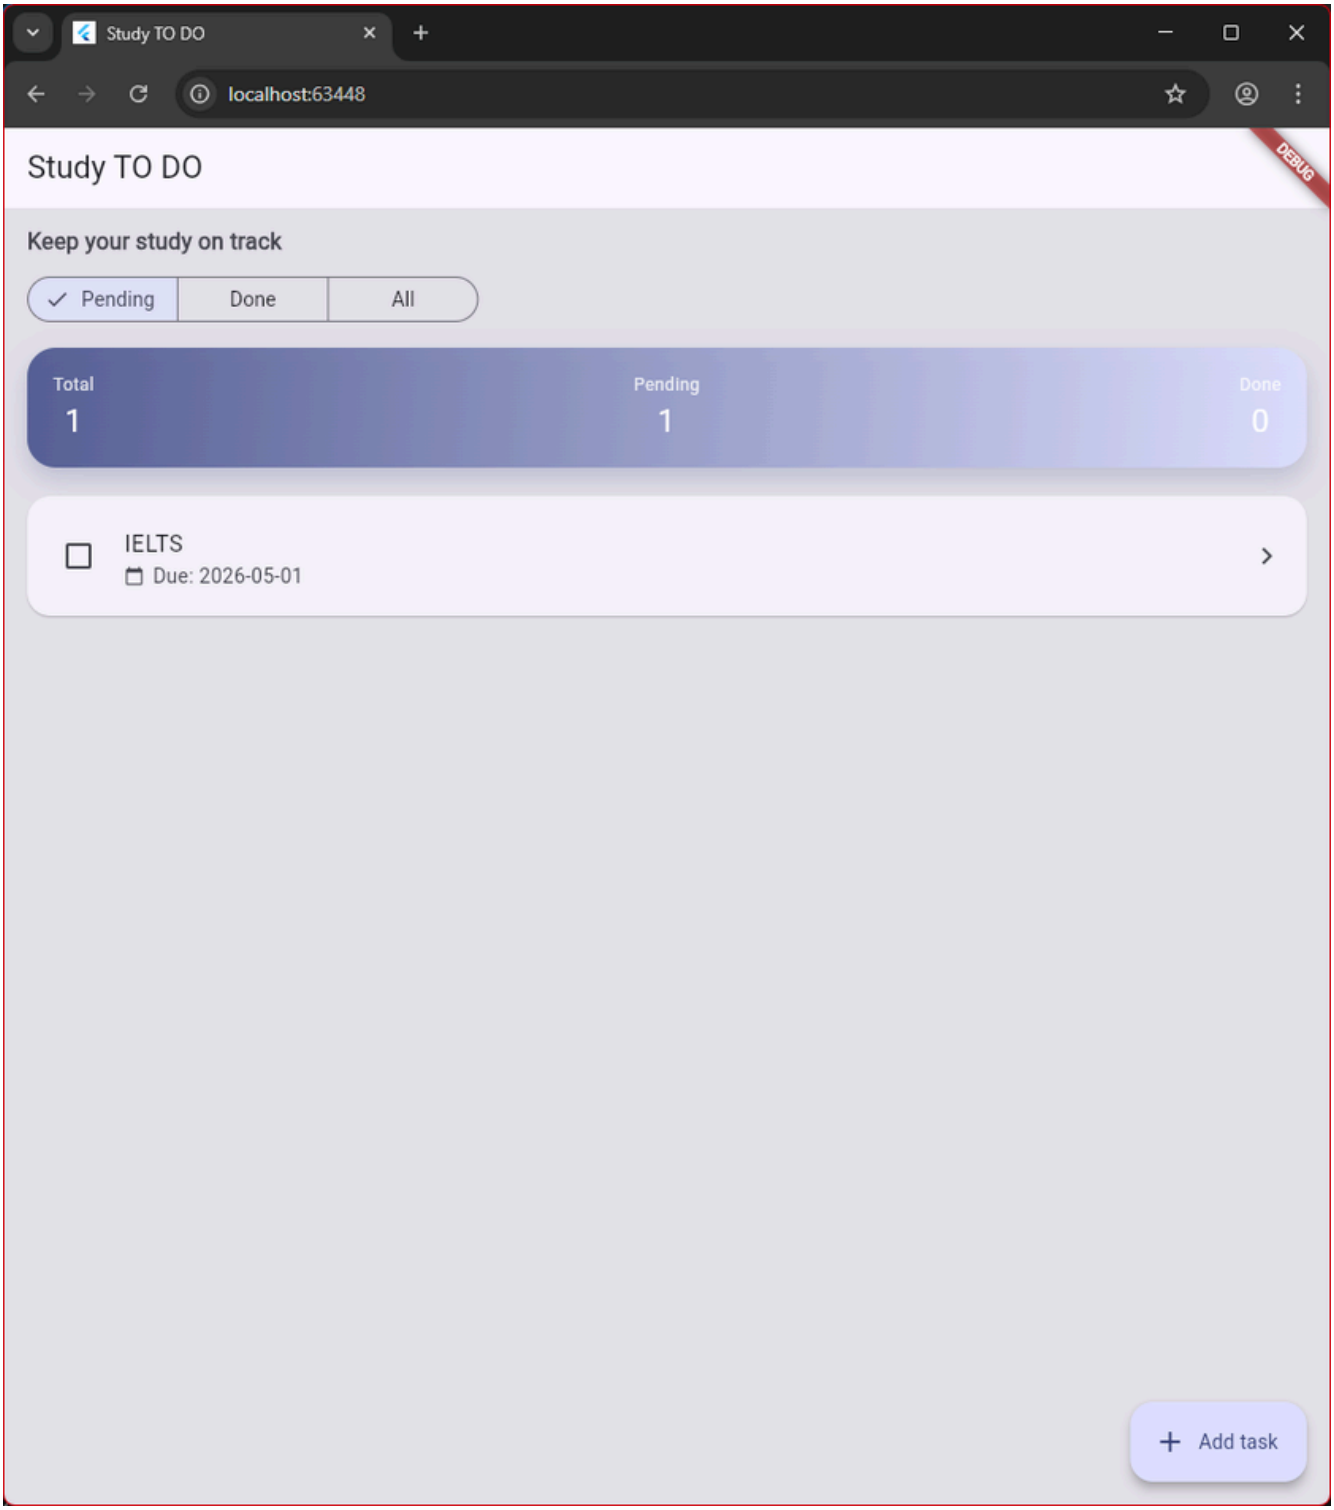
Study TO DO
localhost:63448
Study TO DO
DEBUG
Keep your study on track
Pending
Done
All
Total
1
Pending
1
Done
0
IELTS
Due: 2026-05-01
Add task

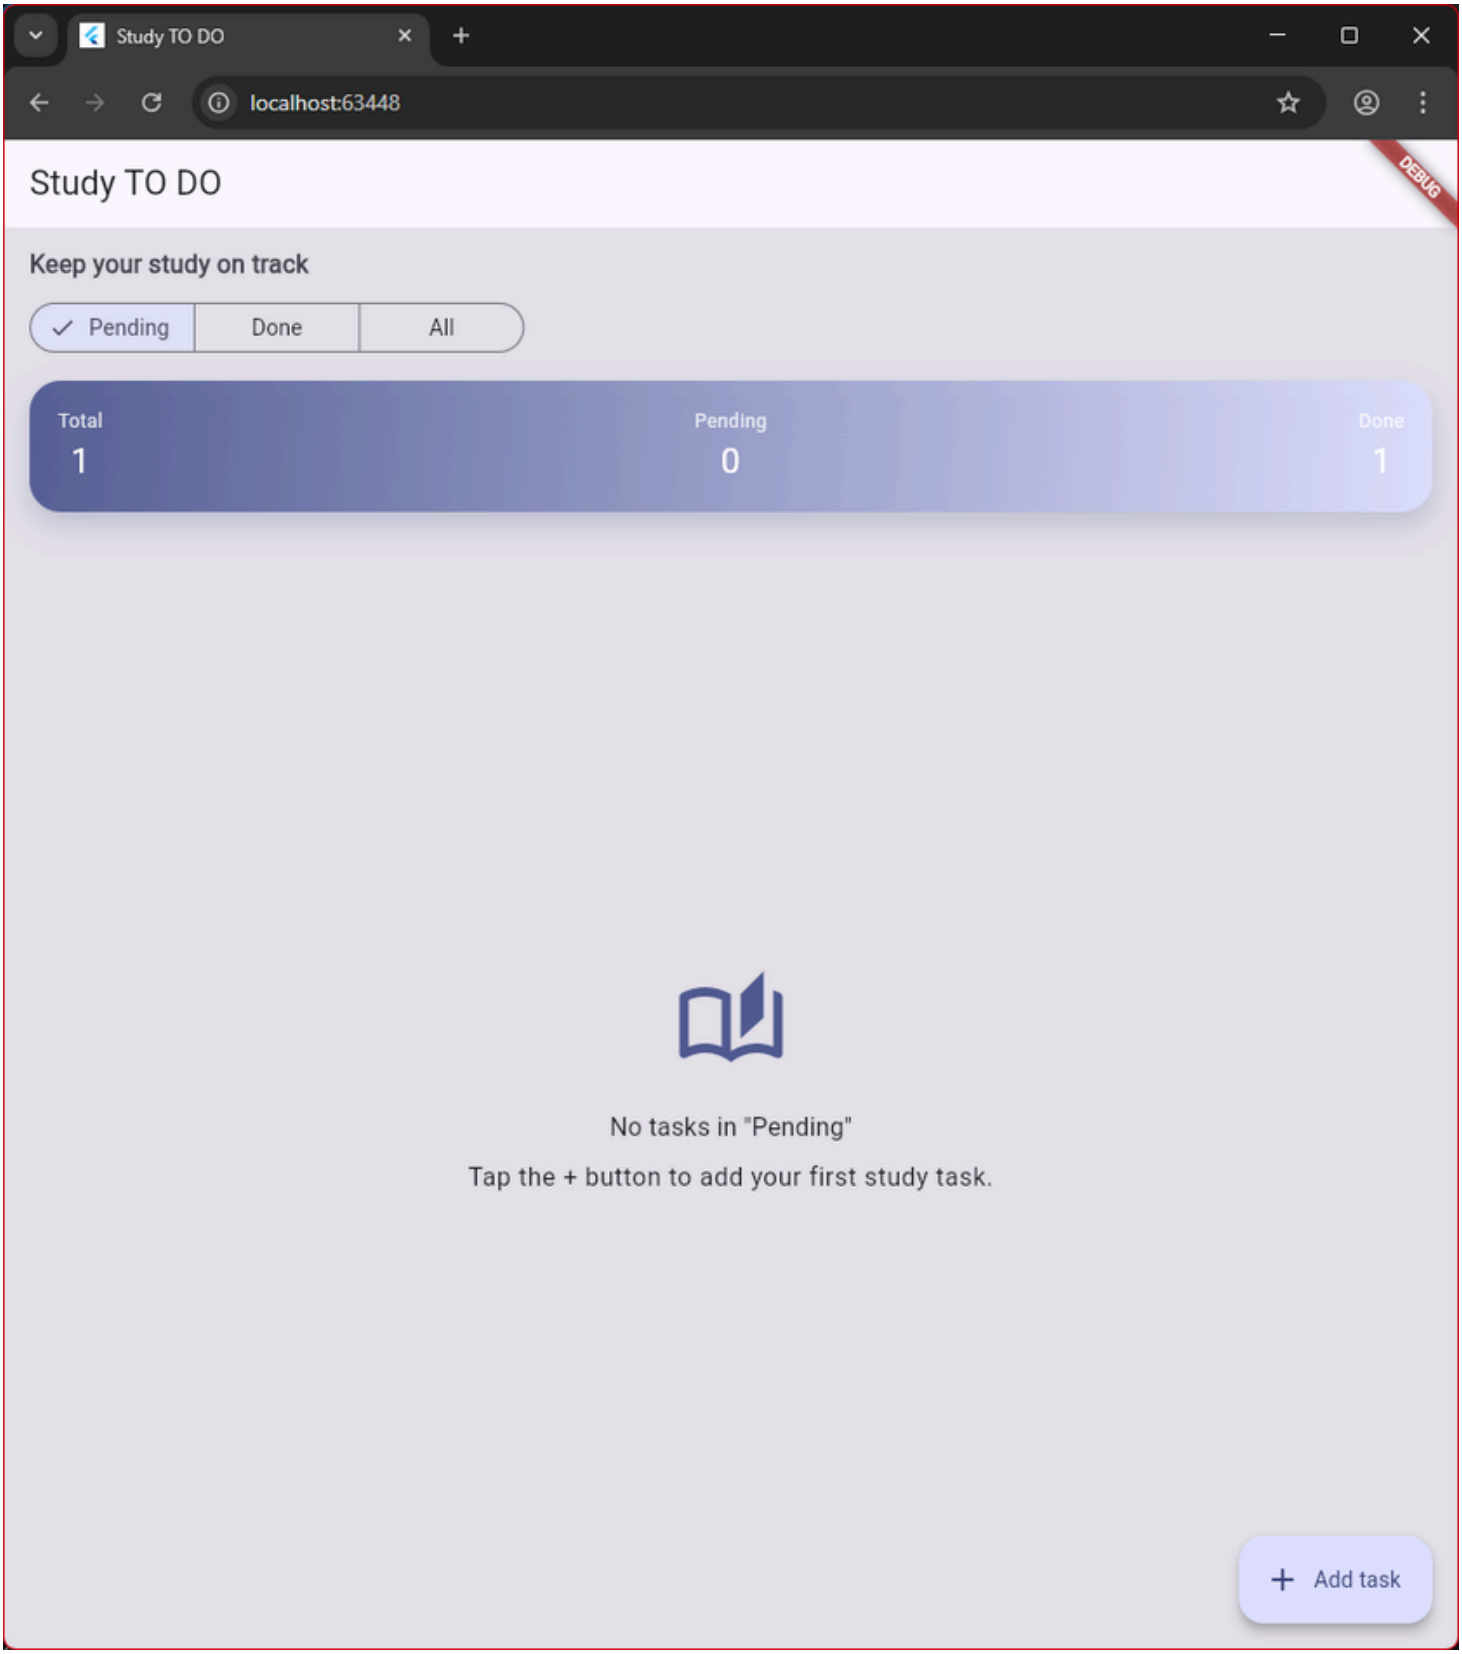
Study TO DO
localhost:63448
Study TO DO
DEBUG
Keep your study on track
Pending
Done
All
Total
1
Pending
0
Done
1
No tasks in "Pending"
Tap the + button to add your first study task.
Add task

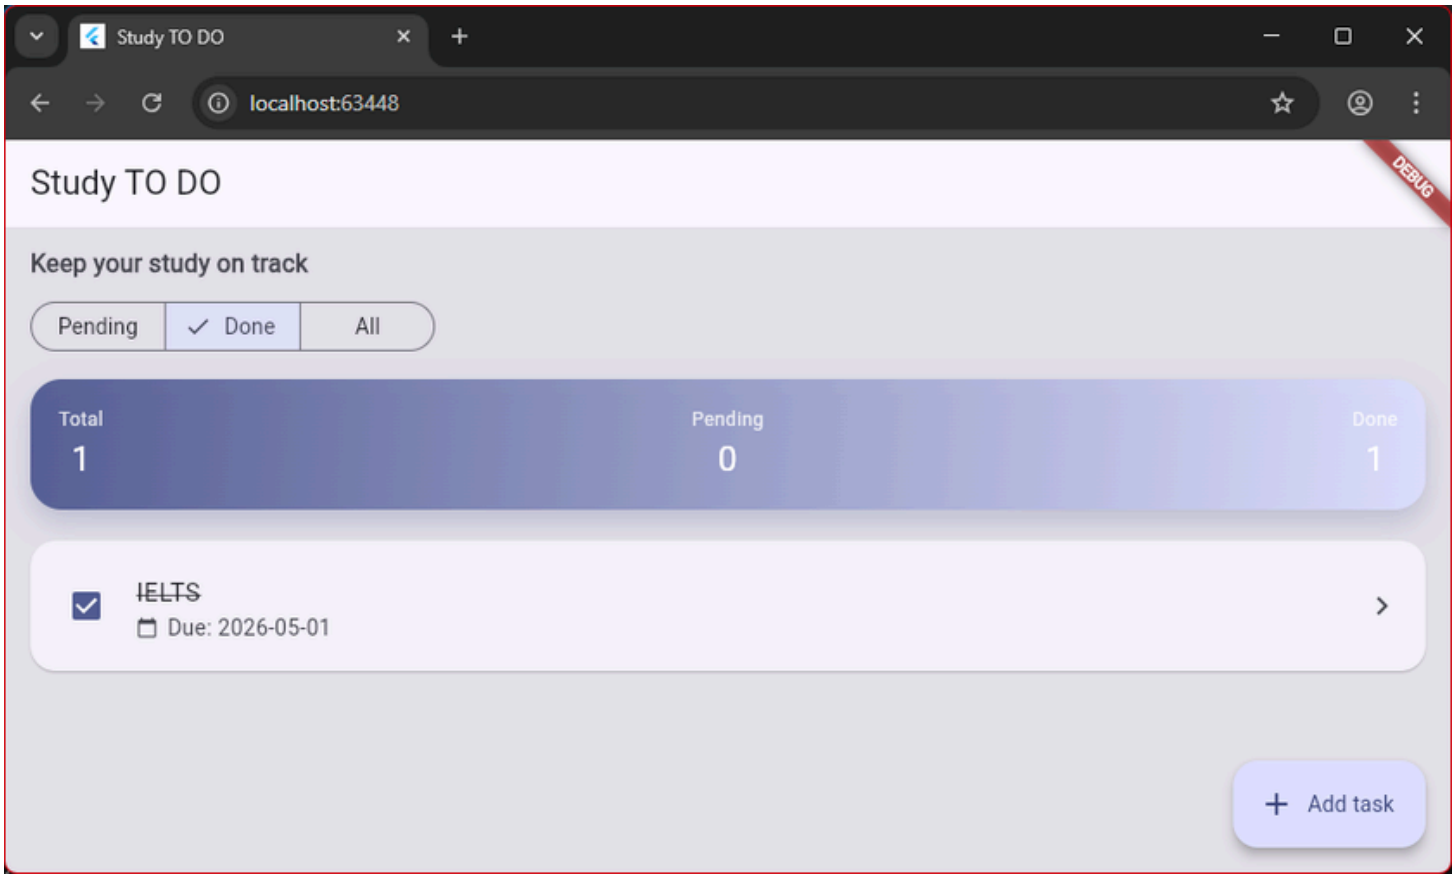
Study TO DO
localhost:63448
Study TO DO
DEBUG
Keep your study on track
Pending
Done
All
Total
1
Pending
0
Done
1
IELTS
Due: 2026-05-01
Add task

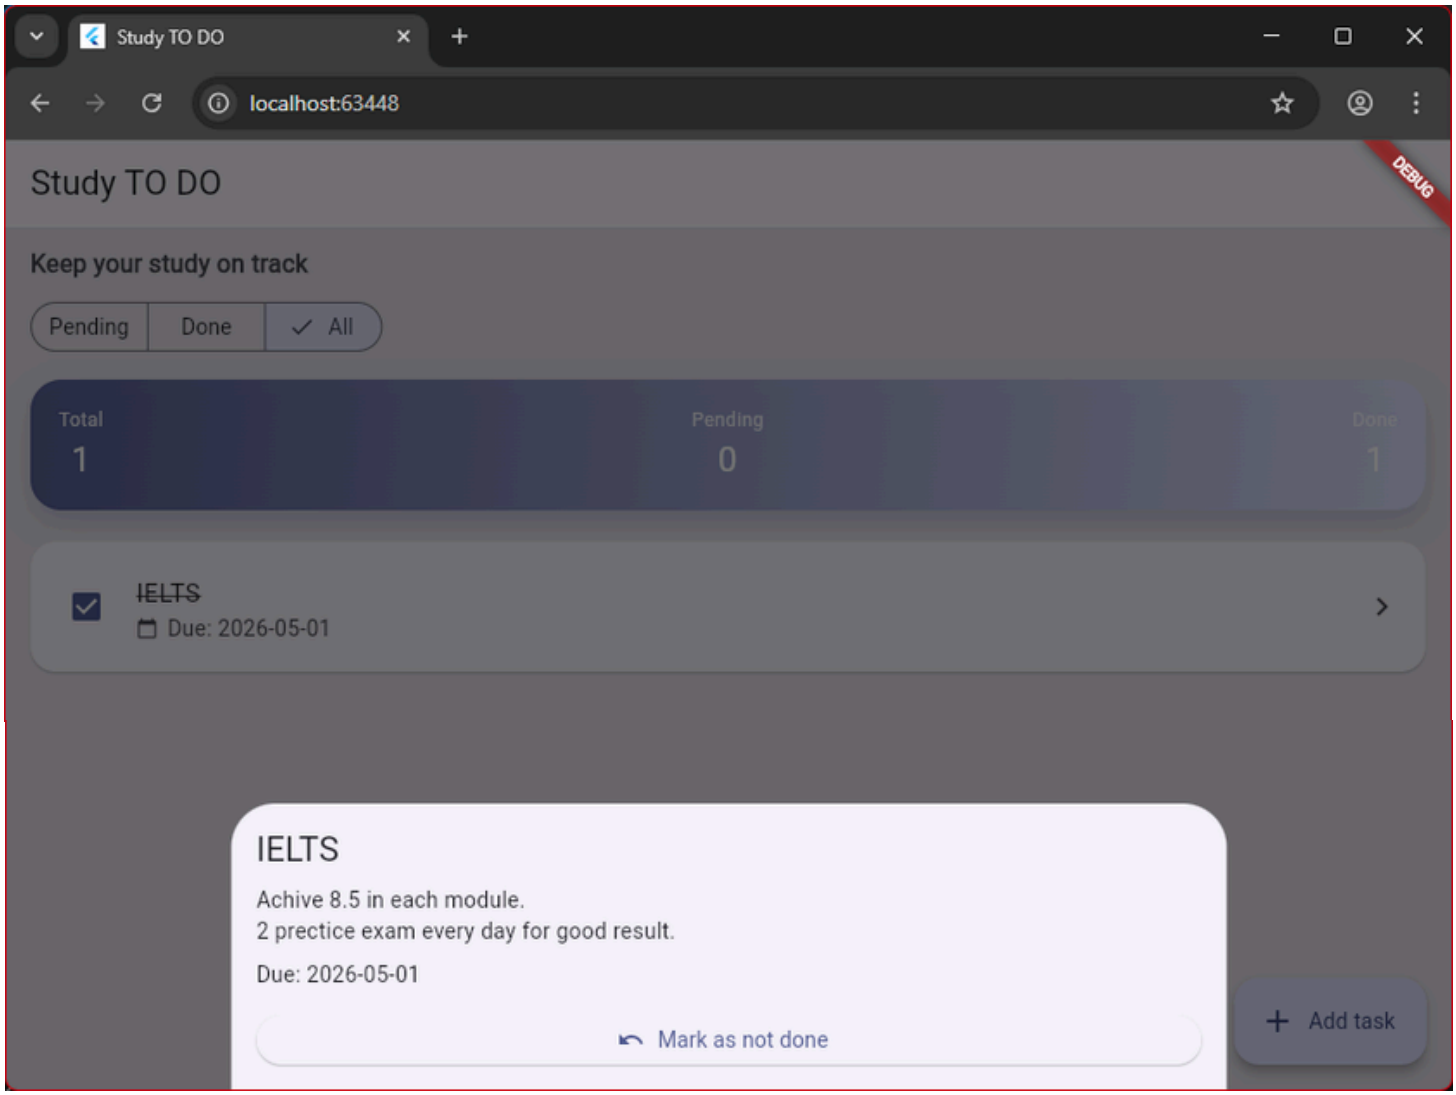
Study TO DO
localhost:63448
Study TO DO
DEBUG
Keep your study on track
Pending
Done
All
Total
1
Pending
0
Done
1
IELTS
Due: 2026-05-01
IELTS
Achive 8.5 in each module.
2 prectice exam every day for good result.
Due: 2026-05-01
Mark as not done
Add task

darshil2711/Study-TODO: A Flu

github.com/darsh...

darshil2711 / Study-TODO

Code Issues Pull requests Actions Projects Wiki Security Insights Settings

Study-TODO

Public

Pin Watch 0 Fork 0 Star 0

main Go to file Code

darshil2711 Update README with project... eb6767f · 3 hours ago

android	Initial commit	3 hours ago
ios	Initial commit	3 hours ago
lib	Initial commit	3 hours ago
linux	Initial commit	3 hours ago
macos	Initial commit	3 hours ago
test	Initial commit	3 hours ago
web	Initial commit	3 hours ago
windows	Initial commit	3 hours ago
.gitignore	Initial commit	3 hours ago
.metadata	Initial commit	3 hours ago
README.md	Update README wit...	3 hours ago
analysis_options.yaml	Initial commit	3 hours ago
pubspec.lock	Initial commit	3 hours ago
pubspec.yaml	Initial commit	3 hours ago

README

Study TO DO

> A simple Flutter study planner app to track your learning tasks, set due dates, and keep momentum.

About

A Flutter study planner app for tracking study tasks, due dates, and completion status with local persistence.

Readme
Activity
0 stars
0 watching
0 forks

Releases

No releases published
Create a new release

Packages

No packages published
Publish your first package

Contributors 1

darshil2711

Languages

- C++ 35.0%
- Dart 29.3%
- CMake 28.0%
- Swift 3.1%
- HTML 2.2%
- C 2.1%
- Other 0.3%

Suggested workflows

Based on your tech stack

CMake

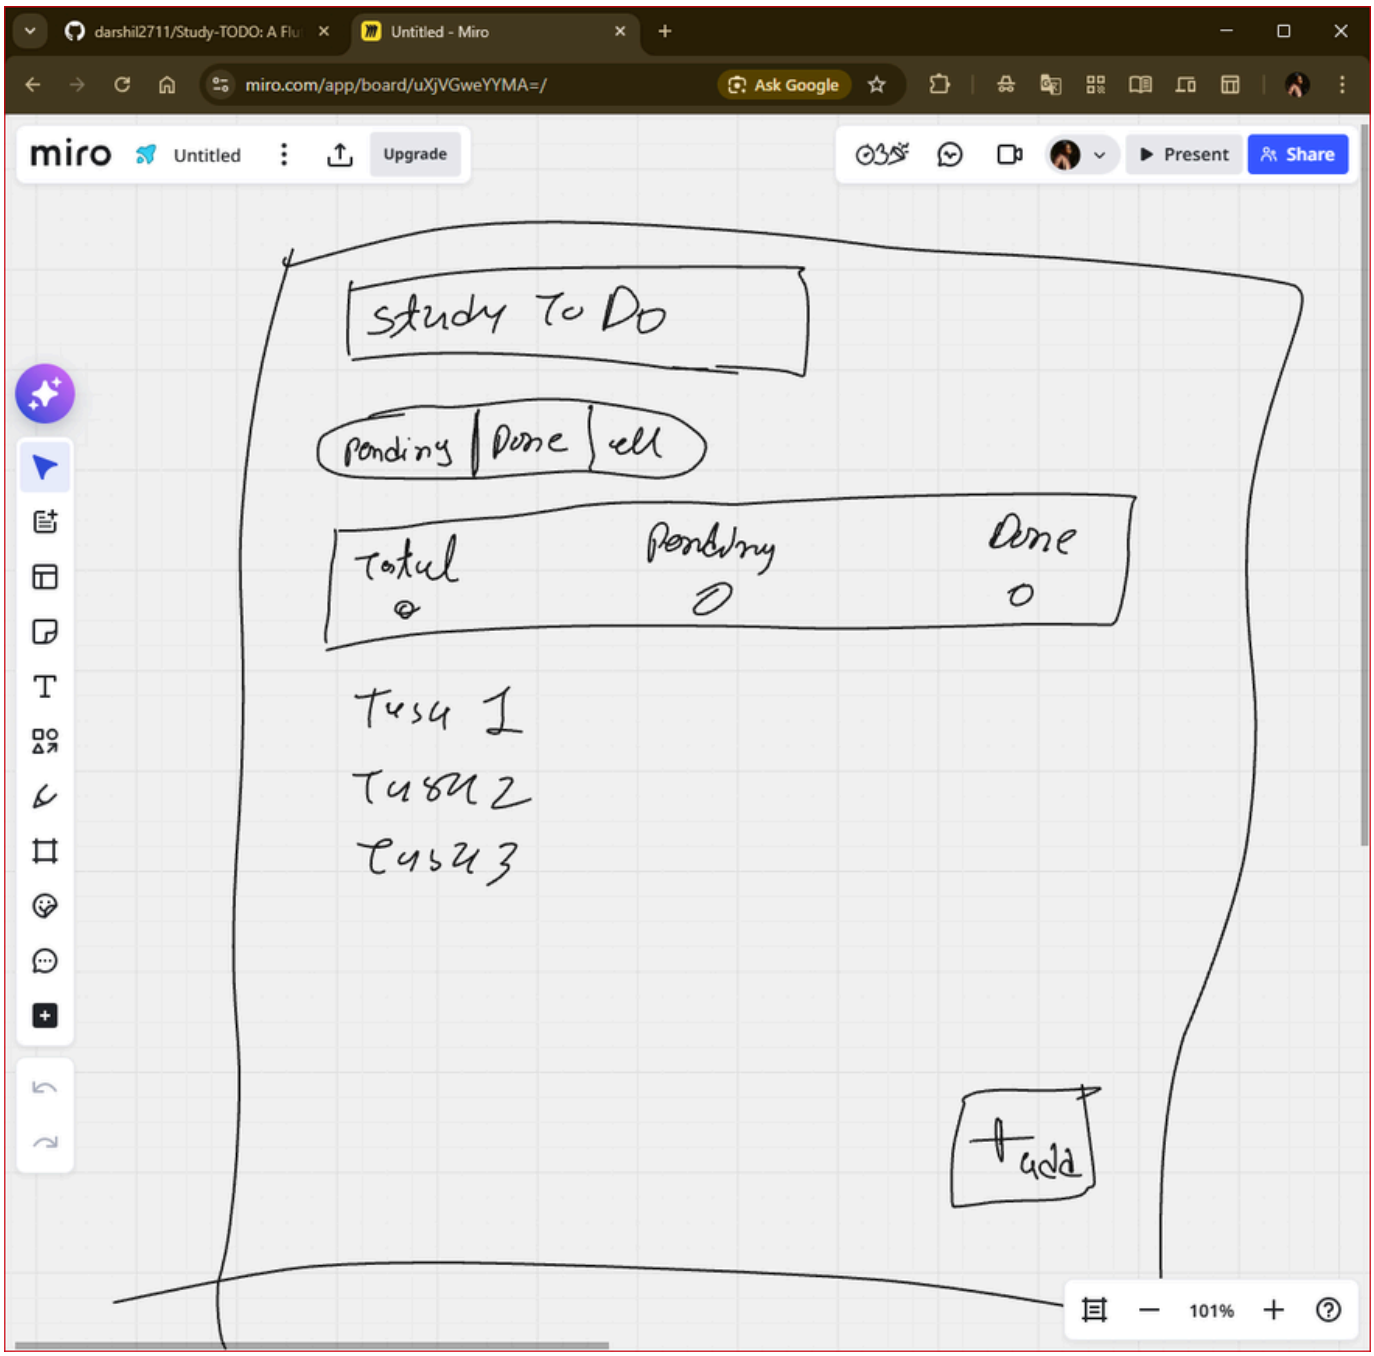
darshil2711/Study-TODO: A Flu
Untitled - Miro
miro.com/app/board/uXjVGweYYMA=/
Ask Google
miro
Untitled
Upgrade
Present
Share
Study To Do
Pending
Done
All
Total
0
Pending
0
Done
0
Task 1
Task 2
Task 3
+ add
101%

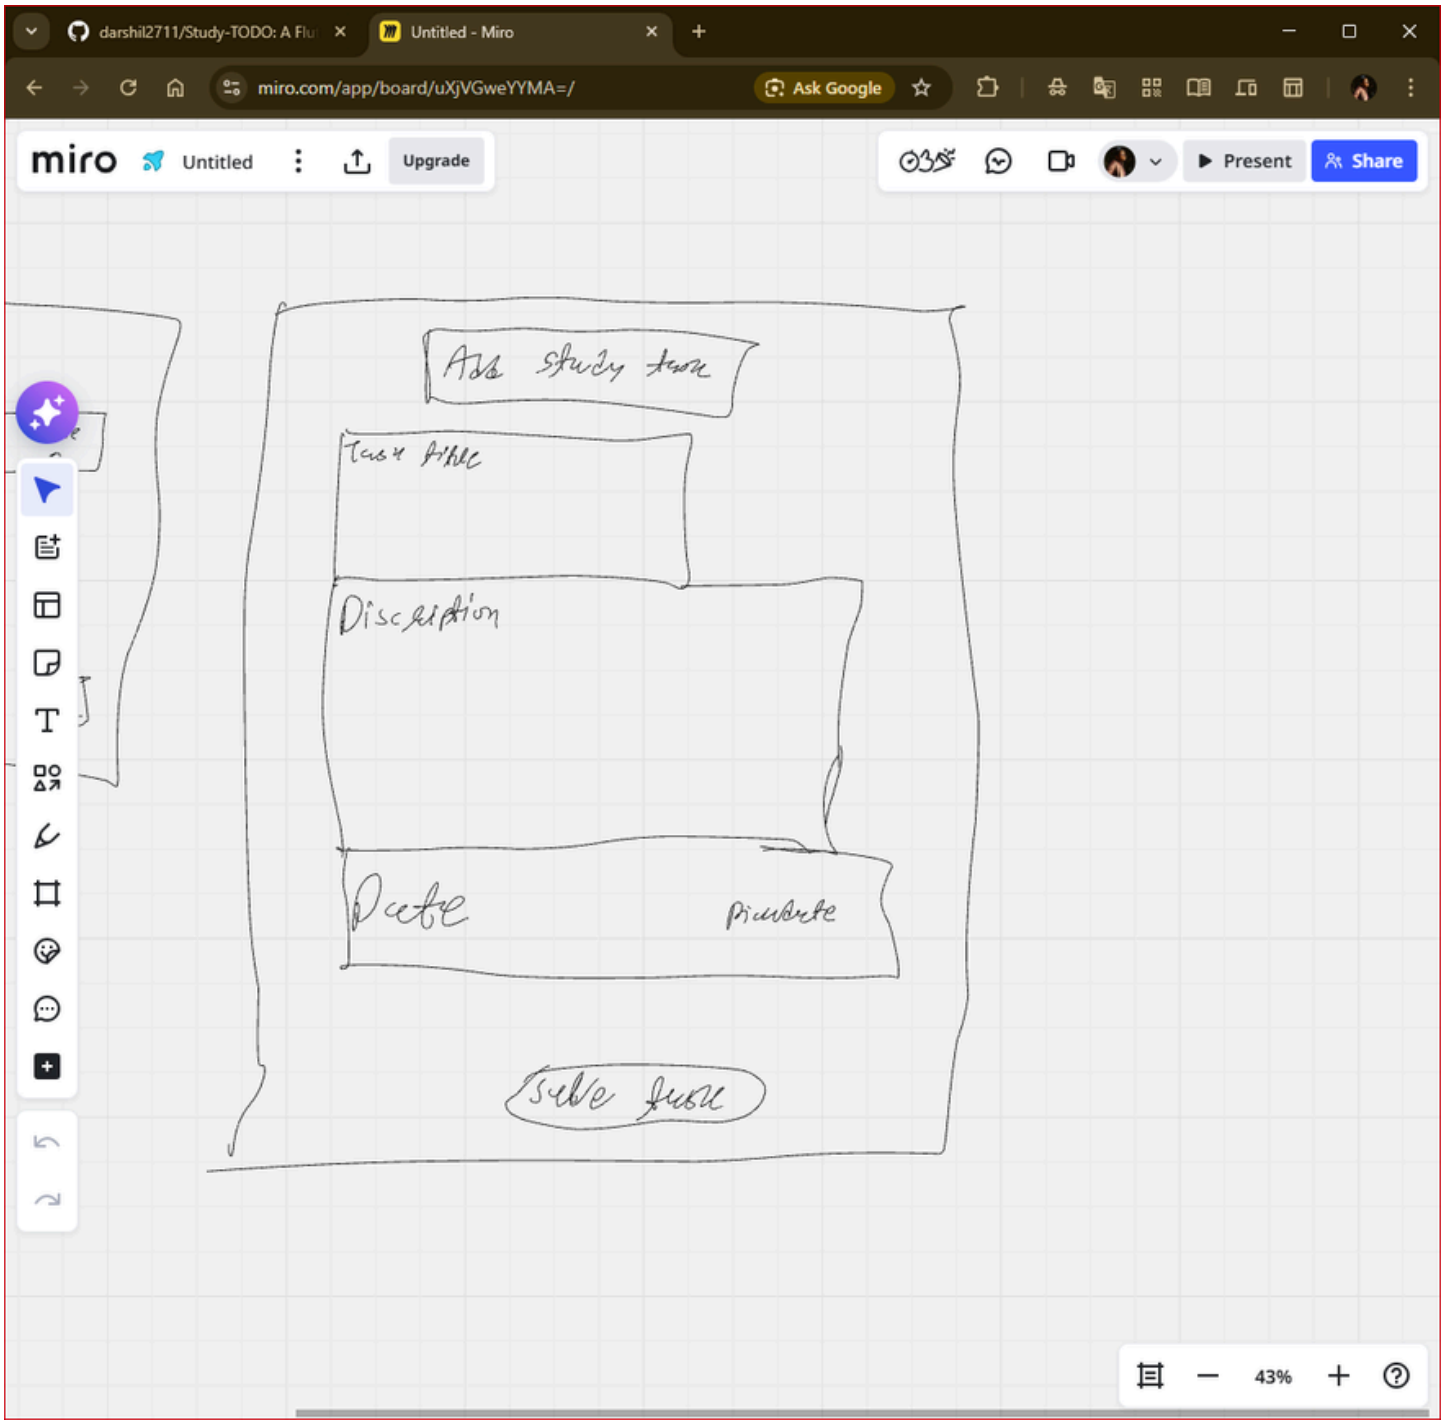
darshil2711/Study-TODO: A Flu
Untitled - Miro
miro.com/app/board/uXjVGweYYMA=/
Ask Google
miro
Untitled
Upgrade
Present
Share
Add study task
Task title
Discription
Date
Priority
Save task
43%
